
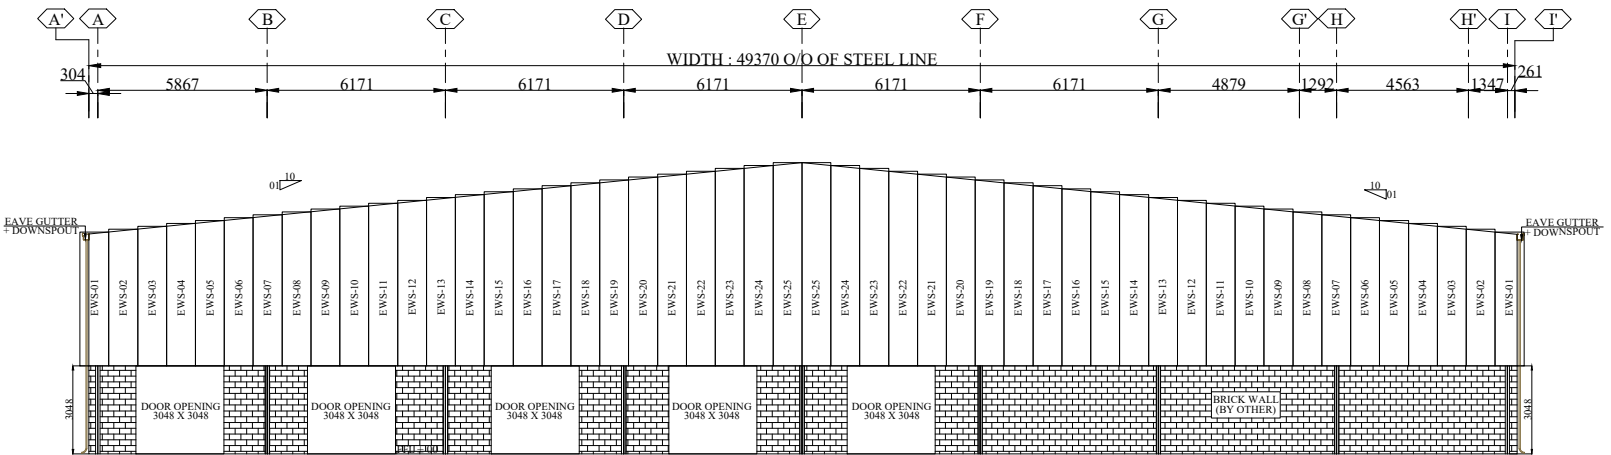


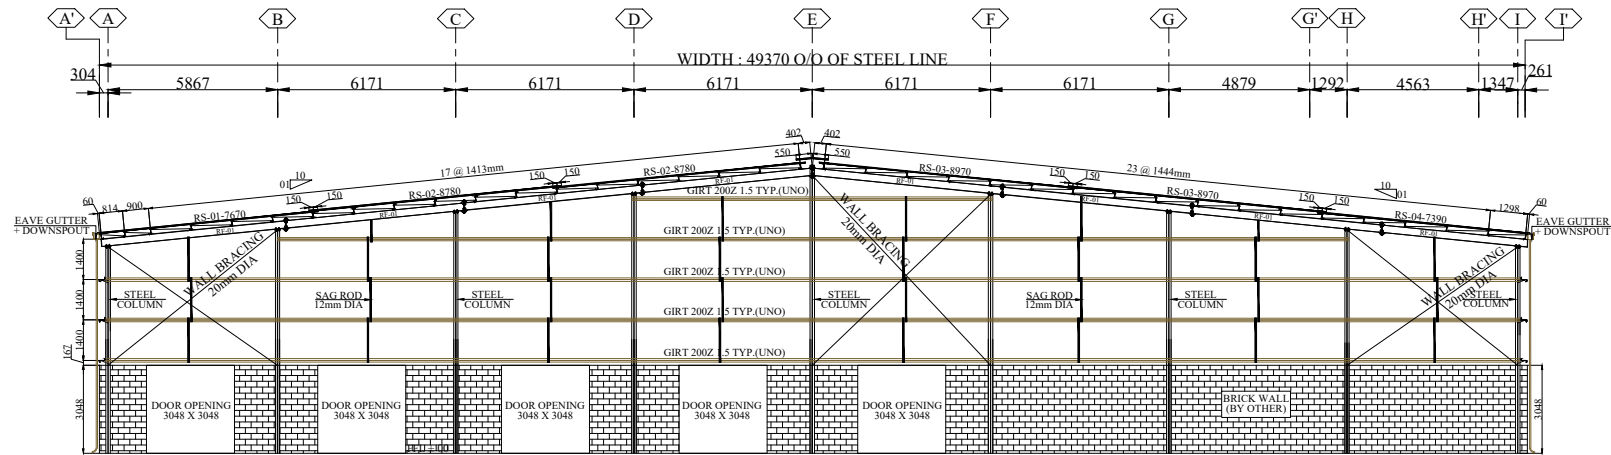

END WALL FRAMING & SHEETING @ G.L 1'

FOR APPROVAL :

IN ORDER TO SCHEDULE THIS PROJECT
IN AN EFFICIENT MANNER , KINDLY
RETURN THESE DRAWINGS WITH YOUR
ANY CHANGES MADE AFTER THE
COMMENTS MARKED IN RED

APPROVAL OF THESE DRAWINGS MAY
DELAY THE FABRICATION SCHEDULE AND
SUBSEQUENTLY THE DELIVERY OF THE
BUILDING.

PLEASE TICK MARK ONLY ONE OF THE FOLLOWING

- ☐ " APPROVED AS IS "
- ☐ " APPROVED AS NOTED "
- ☐ " RESUBMIT AS NOTED "

APPROVE : _____

SIGNATURE: _____

DATE : _____

END WALL SHEETING

DESCRIPTIONS	PART	LENGTH (MM)	WIDTH (MM)	QUANTITY
END WALL SHEET	EWS-01	4,632	1,000	2
END WALL SHEET	EWS-02	4,732	1,000	2
END WALL SHEET	EWS-03	4,832	1,000	2
END WALL SHEET	EWS-04	4,932	1,000	2
END WALL SHEET	EWS-05	5,032	1,000	2
END WALL SHEET	EWS-06	5,132	1,000	2
END WALL SHEET	EWS-07	5,232	1,000	2
END WALL SHEET	EWS-08	5,332	1,000	2
END WALL SHEET	EWS-09	5,432	1,000	2
END WALL SHEET	EWS-10	5,532	1,000	2
END WALL SHEET	EWS-11	5,632	1,000	2
END WALL SHEET	EWS-12	5,732	1,000	2
END WALL SHEET	EWS-13	5,832	1,000	2
END WALL SHEET	EWS-14	5,932	1,000	2
END WALL SHEET	EWS-15	6,032	1,000	2
END WALL SHEET	EWS-16	6,132	1,000	2
END WALL SHEET	EWS-17	6,232	1,000	2
END WALL SHEET	EWS-18	6,232	1,000	2
END WALL SHEET	EWS-19	6,432	1,000	2
END WALL SHEET	EWS-20	6,532	1,000	2
END WALL SHEET	EWS-21	6,632	1,000	2
END WALL SHEET	EWS-22	6,732	1,000	2
END WALL SHEET	EWS-23	6,832	1,000	2
END WALL SHEET	EWS-24	6,932	1,000	2
END WALL SHEET	EWS-25	7,032	1,000	2

REV	DATE	DESCRIPTION	DRAWN BY	CHK BY	APR BY
00	10/04/2025	ISSUED FOR APPROVAL	M.A	S.R	NAS



MAIMAAR STEEL Pvt.Ltd
238, Raiwind Road, Thokar Niaz Baig, Lahore, Pakistan
E-mail: nasir.abbas@maimaargroup.com
E-mail: maimaar.steel@gmail.com
Website: www.maimaargroup.com
E-mail: info@maimaargroup.com
Mob-I : +(92-300) 807 4017 ,+(92-333) 807 1115

JOB NO./QUOTE NO.	MSPL-203	BUILDING #	01
PROJECT NAME	WAREHOUSE		
CUSTOMER	DHL		
JOB SITE LOCATION	RAWAT		

END WALL FRAMING & SHEETING @ G.L 1'

DWG NO.

23
