


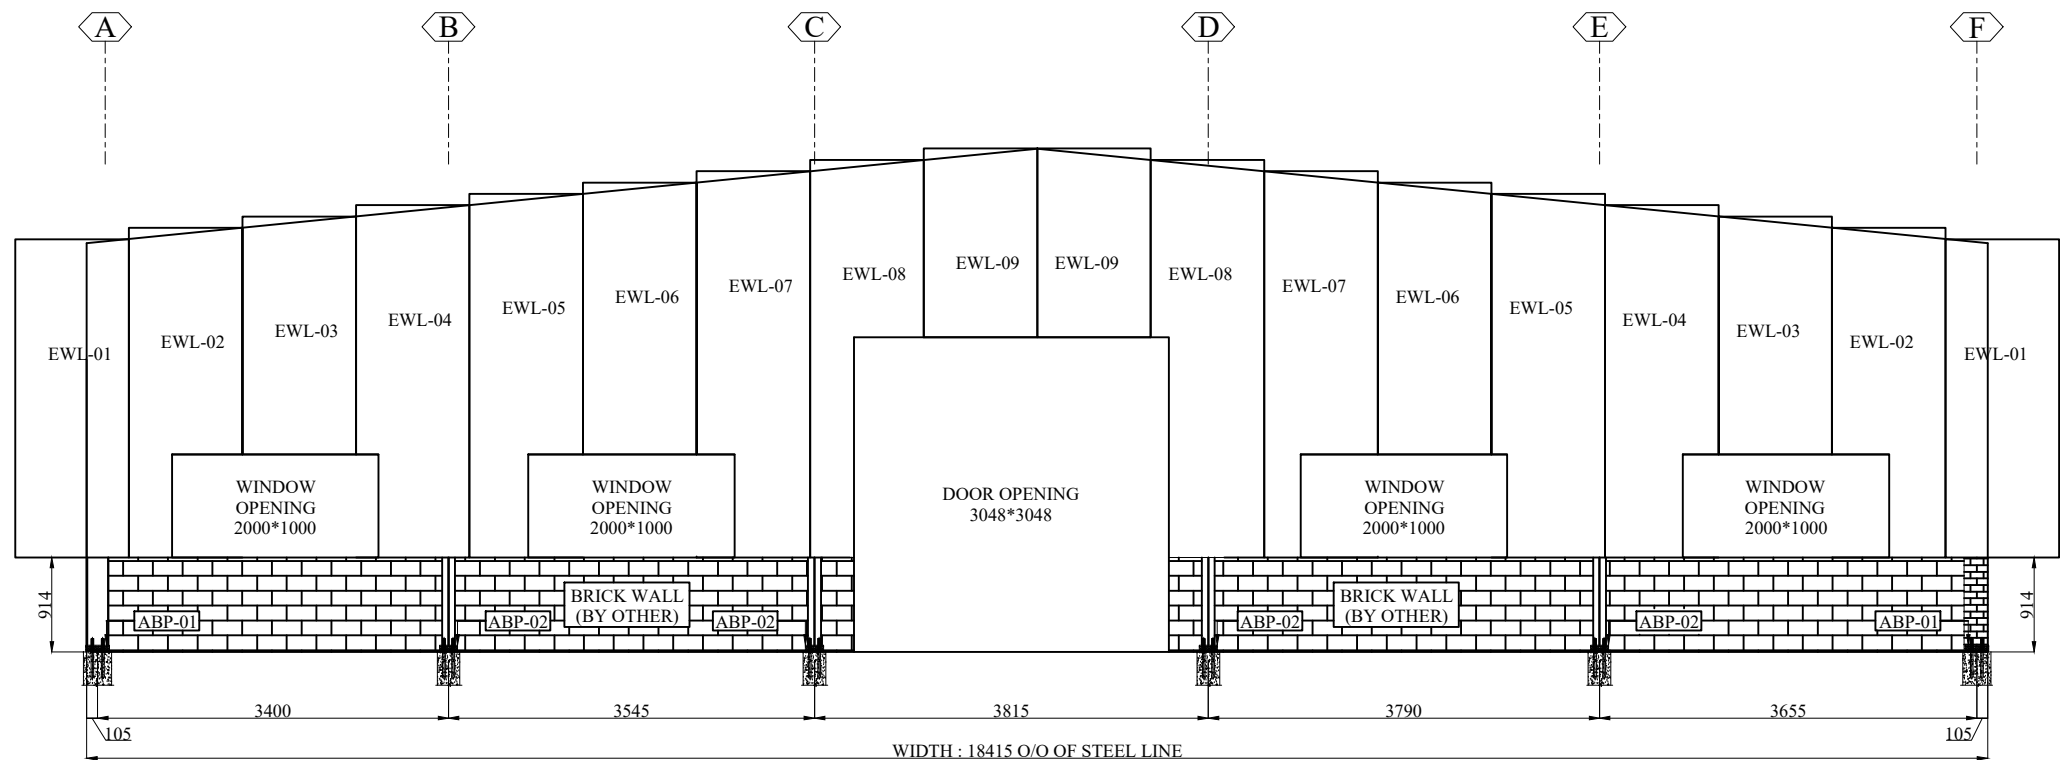

END WALL LINER @ GRID - 01

FOR APPROVAL :

IN ORDER TO SCHEDULE THIS PROJECT IN AN EFFICIENT MANNER , KINDLY RETURN THESE DRAWINGS WITH YOUR COMMENTS MARKED IN RED

APPROVAL OF THESE DRAWINGS MAY DELAY THE FABRICATION SCHEDULE AND SUBSEQUENTLY THE DELIVERY OF THE BUILDING.

PLEASE TICK MARK ONLY ONE OF THE FOLLOWING

☐ " APPROVED AS IS "

☐ " APPROVED AS NOTED"

☐ " RESUBMIT AS NOTED "

APPROVE : _____

SIGNATURE: _____

DATE : _____

END WALL LINER @ GL - 01

DESCRIPTIONS	PART	LENGT H (MM)	WIDTH (MM)	QUANTIT Y
END WALL LINER	EWL-01	3,082	1,100	2
END WALL LINER	EWL-02	3,192	1,100	2
END WALL LINER	EWL-03	3,302	1,100	2
END WALL LINER	EWL-4	3,412	1,100	2
END WALL LINER	EWL-5	3,522	1,100	2
END WALL LINER	EWL-6	3,632	1,100	2
END WALL LINER	EWL-7	3,742	1,100	2
END WALL LINER	EWL-8	3,852	1,100	2
END WALL LINER	EWL-9	1,829	1,100	2

00	04-07-25	ISSUED FOR APPROVAL	I.U	S.R	NAS
REV.	DATE	DESCRIPTION	DRWN BY	CHK BY	APR BY



MAIMAAR STEEL Pvt.Ltd
238, Raiwind Road, Thokar Niaz Baig ,LAHORE, Pakistan
E-mail: nasir.abbas@maimaargroup.com
E-mail: maimaar.steel@gmail.com
Website: www.maimaargroup.com
E-mail: nasir.abbas@maimaargroup.com
Mob-1 : +(92-300) 807 4017 ,+(92-333) 807 1115

JOB NO.	MSPL-187	BLDG #.	01
PROJECT NAME	SUPPLY & INSTALLATION OF PE STEEL PRINTING HALL		
CUSTOMER	BONZER SPORTS		
JOBSITE LOCATION	SIALKOT		

END WALL LINER @ GRID - 01

DWG. NO.
