



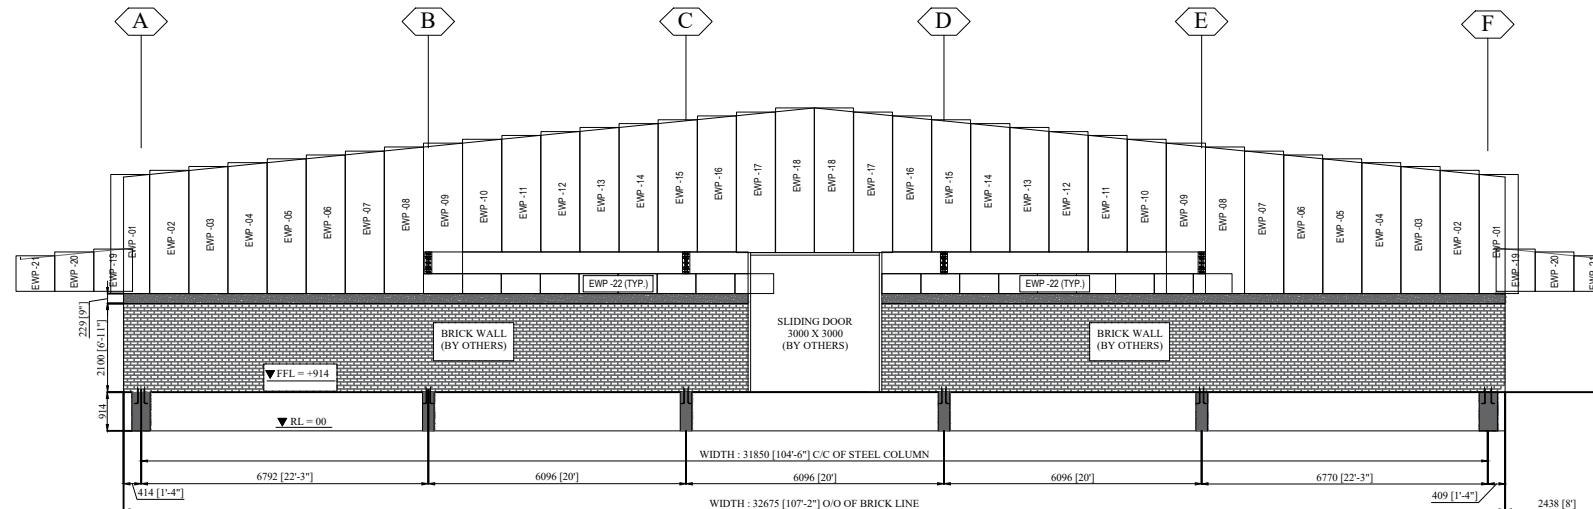

END WALL PANELS

DESCRIPTIONS	PART	LENGTH (MM)	WIDTH (MM)	QUANTITY
END WALL PANEL	EWP-01	2,822	920	2
END WALL PANEL	EWP-02	2,914	920	2
END WALL PANEL	EWP-03	3,006	920	2
END WALL PANEL	EWP-04	3,099	920	2
END WALL PANEL	EWP-05	3,191	920	2
END WALL PANEL	EWP-06	3,283	920	2
END WALL PANEL	EWP-07	3,376	920	2
END WALL PANEL	EWP-08	3,468	920	2
END WALL PANEL	EWP-09	3,560	920	2
END WALL PANEL	EWP-10	2,668	920	2
END WALL PANEL	EWP-11	2,760	920	2
END WALL PANEL	EWP-12	2,852	920	2
END WALL PANEL	EWP-13	2,945	920	2
END WALL PANEL	EWP-14	3,037	920	2
END WALL PANEL	EWP-15	3,129	920	2
END WALL PANEL	EWP-16	3,222	920	2
END WALL PANEL	EWP-17	3,325	920	2
END WALL PANEL	EWP-18	3,418	920	2
END WALL PANEL	EWP-19	1,006	920	1
END WALL PANEL	EWP-20	936	920	1
END WALL PANEL	EWP-21	844	920	1
END WALL PANEL	EWP-22	473	920	18

REV	DATE	DESCRIPTION	DRAWN BY	CHK BY	APR BY
03	20-Jun-24	ISSUED FOR APPROVAL	IU	KAS	NAS

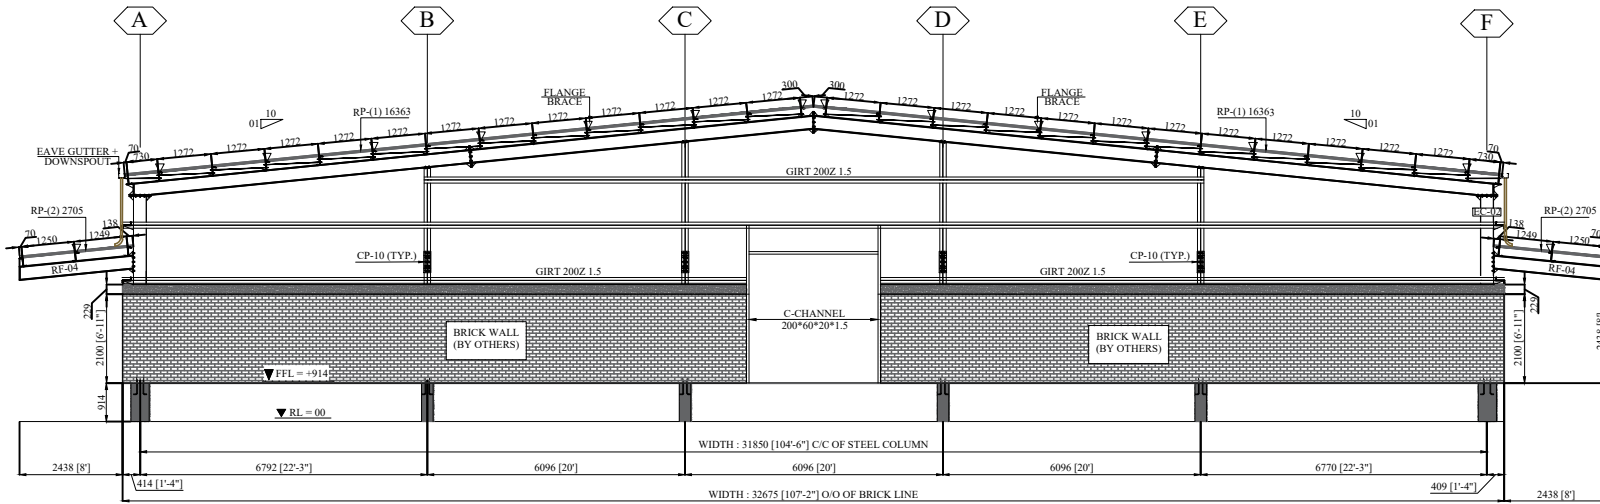

MAIMAAR STEEL Pvt.Ltd
 238, Raiwind Road, Thokar Niaz Baig, Lahore, Pakistan
 E-mail: nasir.abbas@maimaargroup.com
 E-mail: maimaar.steel@gmail.com
 Website: www.maimaargroup.com
 E-mail: info@maimaargroup.com
 Mob-I : +(92-300) 807 4017 ,+(92-333) 807 1115

JOB NO./QUOTE NO.	MSPL-135	BUILDING #	01
PROJECT NAME	DRY FRUITS PROCESSING DERA ISMAIL KHAN		
CUSTOMER	45 ENGINEER DIVISION		
JOB SITE LOCATION	DERA ISMAIL KHAN		

END WALL FRAMING & SHEETING @ GRID 07

DWG NO.
E09

END WALL FRAMING & SHEETING @ GRID 07

FOR APPROVAL :

IN ORDER TO SCHEDULE THIS PROJECT IN AN EFFICIENT MANNER , KINDLY RETURN THESE DRAWINGS WITH YOUR ANY CHANGES MADE AFTER THE COMMENTS MARKED IN RED

APPROVAL OF THESE DRAWINGS MAY DELAY THE FABRICATION SCHEDULE AND SUBSEQUENTLY THE DELIVERY OF THE BUILDING.

PLEASE TICK MARK ONLY ONE OF THE FOLLOWING

- ☐ " APPROVED AS IS "
☐ " APPROVED AS NOTED "
☐ " RESUBMIT AS NOTED "

APPROVE : _____

SIGNATURE: _____

DATE : _____
