



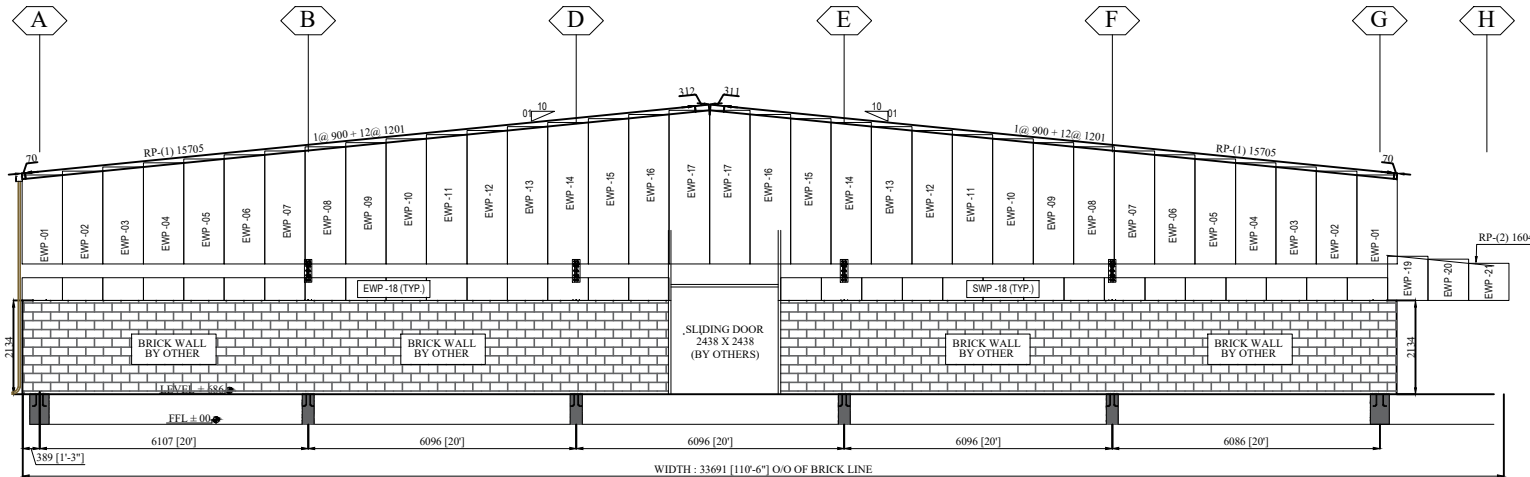

END WALL PANELS

DESCRIPTIONS	PART	LENGTH (MM)	WIDTH (MM)	QUANTITY
END WALL PANEL	EWP-01	2,023	920	2
END WALL PANEL	EWP-02	2,115	920	2
END WALL PANEL	EWP-03	2,207	920	2
END WALL PANEL	EWP-04	2,299	920	2
END WALL PANEL	EWP-05	2,391	920	2
END WALL PANEL	EWP-06	2,482	920	2
END WALL PANEL	EWP-07	2,574	920	2
END WALL PANEL	EWP-08	2,666	920	2
END WALL PANEL	EWP-09	2,758	920	2
END WALL PANEL	EWP-10	2,850	920	2
END WALL PANEL	EWP-11	2,942	920	2
END WALL PANEL	EWP-12	3,034	920	2
END WALL PANEL	EWP-13	3,126	920	2
END WALL PANEL	EWP-14	3,218	920	2
END WALL PANEL	EWP-15	3,310	920	2
END WALL PANEL	EWP-16	3,402	920	2
END WALL PANEL	EWP-17	3,494	920	2
END WALL PANEL	EWP-18	519	920	31
END WALL PANEL	EWP-19	1,006	920	1
END WALL PANEL	EWP-20	936	920	1
END WALL PANEL	EWP-21	844	920	1

REV	DATE	DESCRIPTION	DRAWN BY	CHK BY	APR BY
00	10-Jun-24	ISSUED FOR APPROVAL	MA	KAS	NAS

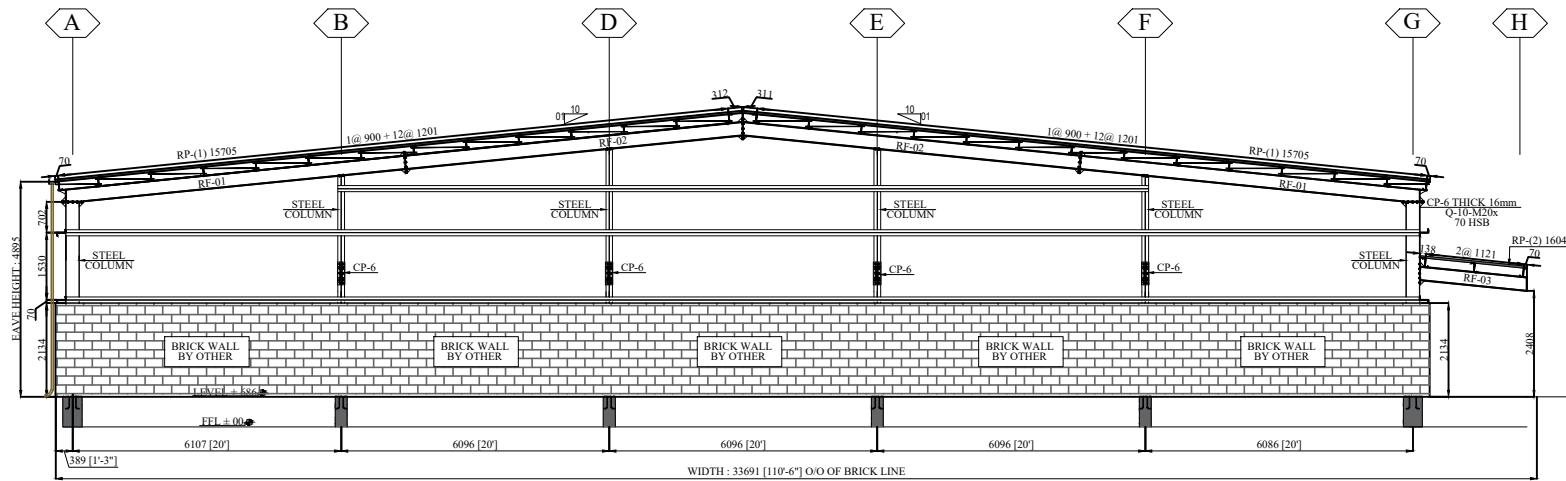

MAIMAAR STEEL Pvt.Ltd
 238, Raiwind Road, Thokar Niaz Baig, Lahore, Pakistan
 E-mail: nasir.abbas@maimaargroup.com
 E-mail: maimaar.steel@gmail.com
 Website: www.maimaargroup.com
 E-mail: info@maimaargroup.com
 Mob-1 : +(92-300) 807 4017, +(92-333) 807 1115

JOB NO./QUOTE NO.	MSPL-135	BUILDING #	01
PROJECT NAME	DRY FRUITS PROCESSING DERA ISMAIL KHAN		
CUSTOMER	45 ENGINEER DIVISION		
JOB SITE LOCATION	DERA ISMAIL KHAN		

END WALL FRAMING & SHEETING @ GRID 07

DWG NO.

14

END WALL FRAMING & SHEETING @ GRID 07

FOR APPROVAL :

IN ORDER TO SCHEDULE THIS PROJECT IN AN EFFICIENT MANNER, KINDLY RETURN THESE DRAWINGS WITH YOUR ANY CHANGES MADE AFTER THE COMMENTS MARKED IN RED

APPROVAL OF THESE DRAWINGS MAY DELAY THE FABRICATION SCHEDULE AND SUBSEQUENTLY THE DELIVERY OF THE BUILDING.

PLEASE TICK MARK ONLY ONE OF THE FOLLOWING

- ☐ " APPROVED AS IS "
☐ " APPROVED AS NOTED "
☐ " RESUBMIT AS NOTED "

APPROVE : _____

SIGNATURE : _____

DATE : _____
